Project Planning Phase
Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	2 October 2026
Team ID	
Project Name	Streamlining IT Procurement: Automating Standard Laptop Orders with Flow Designer
Maximum Marks	4 Marks

Product Backlog, Sprint Schedule, and Estimation:

The product backlog contains all the stories the team needs to deliver for Streamlining IT Procurement: Automating Standard Laptop Orders with Flow Designer. The stories are split across three sprints of 6 days each, with story point estimates and a priority for every item.


Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Setup and configuration	USN-10	As a developer, I can set up the standard laptop catalog item, its variables and the required user roles in ServiceNow.	5	High	Team Member 1
Sprint-1	Laptop request	USN-1	As an employee, I can pick a standard laptop from the service catalog and send in my request.	5	High	Team Member 2
Sprint-1	Approval	USN-4	As a manager, I can approve or decline a laptop request with a single click from email or my phone.	5	High	Team Member 3
Sprint-2	Request tracking	USN-2	As an employee, I can check where my laptop request currently stands.	3	Medium	Team Member 2
Sprint-2	Notifications	USN-3	As an employee, I get notified once my request is approved, dispatched and delivered.	3	Medium	Team Member 4
Sprint-2	Approval	USN-5	As a manager, I am spared from approving standard requests raised by pre-approved roles.	5	High	Team Member 3
Sprint-2	Fulfilment	USN-6	As a coordinator, I want inventory to be verified and a laptop reserved without manual effort.	5	High	Team Member 1
Sprint-2	Purchasing	USN-7	As a coordinator, I want a purchase order raised automatically whenever a laptop is not in stock.	5	Medium	Team Member 4
Sprint-3	Asset management	USN-8	As a coordinator, I want an asset record generated and linked to the employee once the laptop is delivered.	5	Medium	Team Member 1
Sprint-3	Reporting	USN-9	As an IT manager, I can see turnaround time and cost savings on a dashboard.	3	Low	Team Member 2
Sprint-3	Testing and release	USN-11	As a project team, we validate the complete flow using sample requests and then release it to users.	8	High	All team members

Project Tracker, Velocity & Burndown Chart:

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	15	6 Days	03 Feb 2025	08 Feb 2025	15	08 Feb 2025
Sprint-2	21	6 Days	10 Feb 2025	15 Feb 2025	21	15 Feb 2025
Sprint-3	16	6 Days	17 Feb 2025	22 Feb 2025	16	22 Feb 2025

Velocity: The team has planned 52 story points across 3 sprints of 6 days each (18 days in total). This gives an average velocity of 52 / 3 = about 17.3 story points per sprint, or 52 / 18 = about 2.9 story points per day.

Burndown chart: The chart plots the story points left at the beginning of the project and at the close of each sprint. The planned progress stays very close to the ideal line.

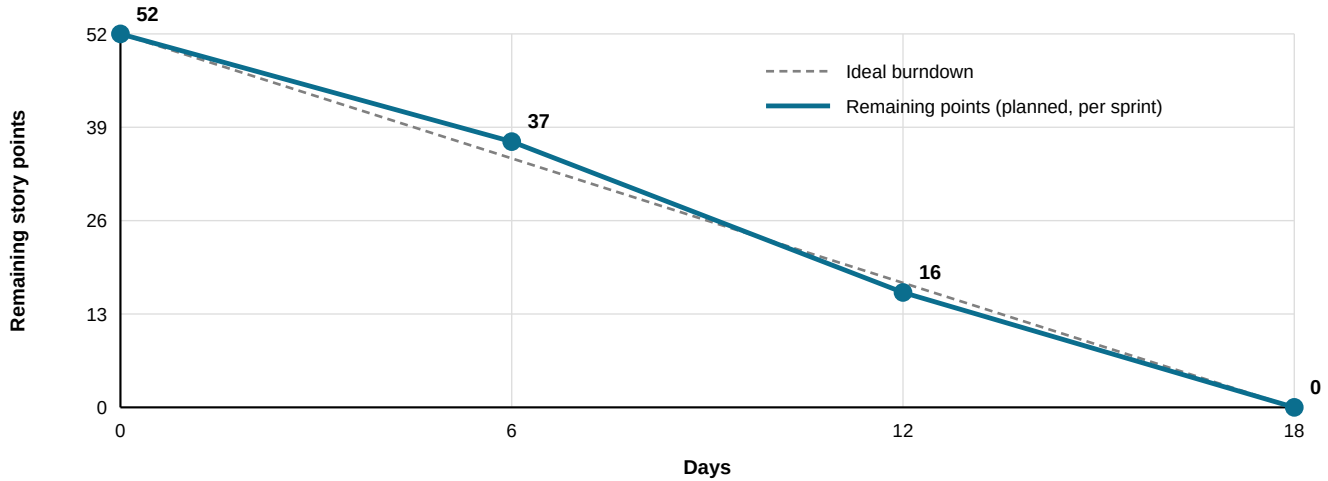

Implementation Screenshots (ServiceNow)

Captured from the project demo video: Flow Designer build and a test laptop request.




Figure 1: Catalog item "Standard Laptop" (Lenovo Carbon x1) in the catalog




Figure 2: Flow Designer: Service Catalog trigger and Create Catalog Task action




Figure 3: Standard Laptop order page with Order Now




Figure 4: Approval record for REQ0010001 (Approve / Reject)




Figure 5: Catalog task SCTASK0010001 "Laptop need to Configure"
